

Construction Weekly Update

Week of January 6th, 2020


School District of Manawa



Continued masonry at Addition C



Installed blocking at Addition C Restrooms

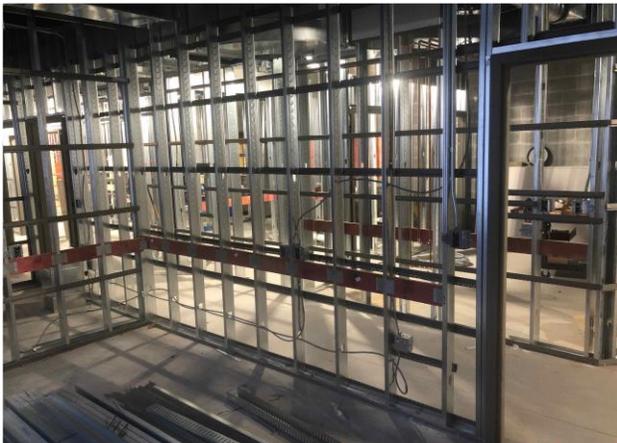

Continued electrical rough-in at Addition C



Installed ductwork in Addition C

Update

Fire wall and elevator shaft masonry work in Addition A advanced this week in anticipation of steel erection. Steel stud framing, cabinetry blocking, and electrical & mechanical rough-ins continued in Addition C. Exterior spray foam insulation was applied at Addition C.

About Hoffman

Hoffman Planning, Design & Construction, Inc. is an integrated Total Project Management firm based in Appleton, Wisconsin. We partner with our clients to create innovative designs and build high quality, functional, attractive, energy efficient facilities at costs at or below projects delivered using traditional design and construction methods. Currently in our fifth generation of leadership, Hoffman continues to deliver the same expert service and superior value our clients have come to appreciate.
